Harbour Line tram extension

Steering group update · Q3 2027

Project delivery office, Port Calder · meeting of 12 October 2027

Synthetic sample: the project, the city, the people and all figures are invented.

Summary


- Track laying on the Quay Street section is six weeks behind plan.
- Spending to the end of September: £41.2 m of the £118.5 m budget.
- Utility diversions on Ferry Road finished in August, two weeks early.
- The planning committee approved the design of the Calder Market stop.

Status by workstream

WORKSTREAM	STATUS	COMMENT
Utility diversions	On track	Complete; final inspection booked for October
Track works	Late	Second rail delivery delayed by the supplier
Overhead line	At risk	Bridge section design under review
Tram stops	On track	Five of seven platforms poured
Depot extension	At risk	Ground survey received; no piling changes needed

On track · At risk · Late

Spending by workstream to the end of September (£ m)

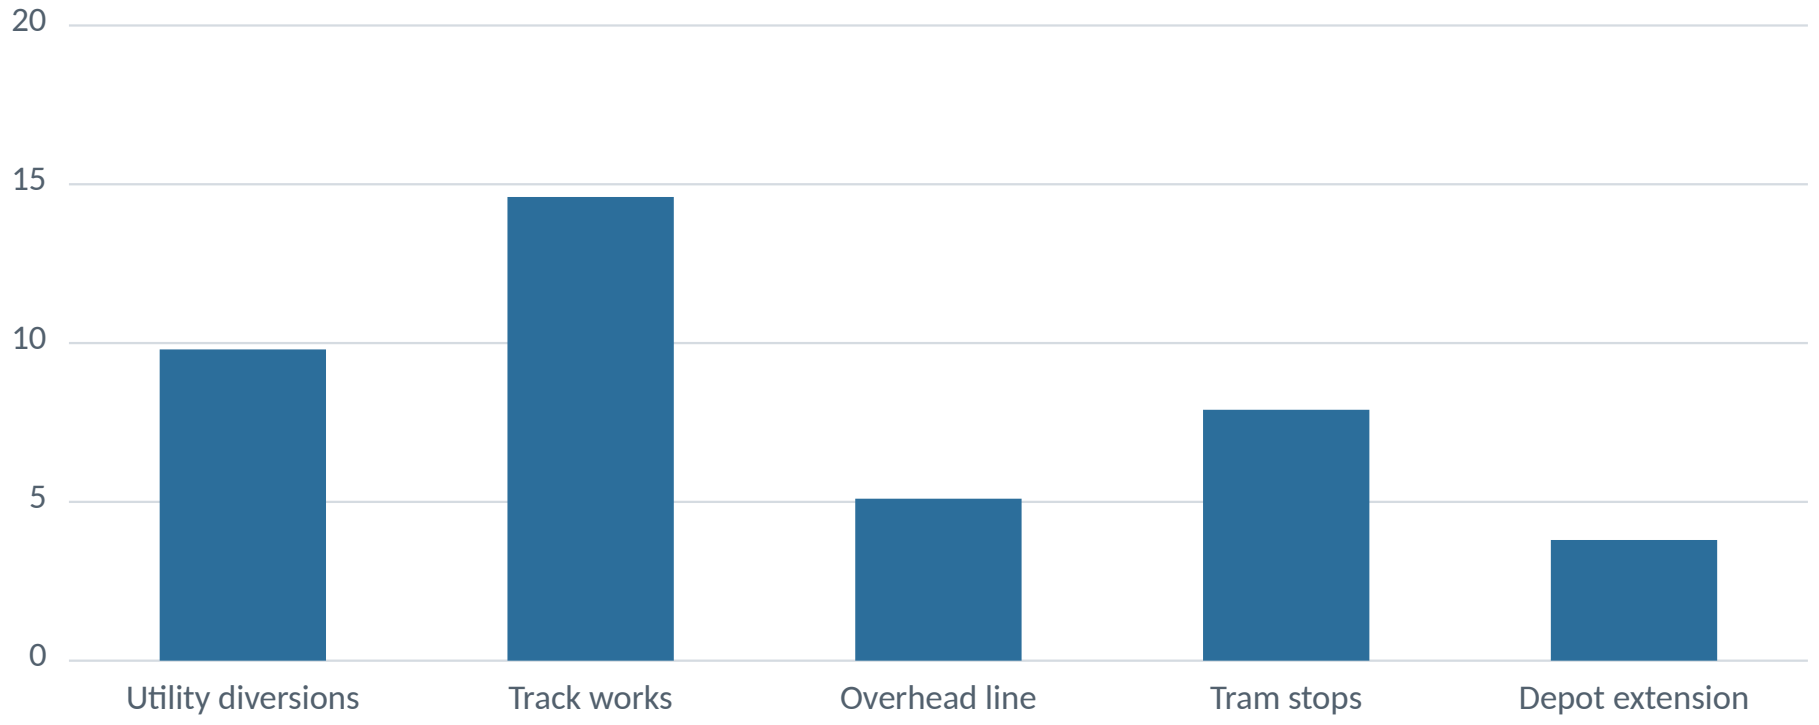

Source: project ledger, 30 September 2027

Top risks

- Rail supply: the second delivery may slip to January.
- Bridge section: the rail operator must approve the overhead line fixings.
- Night works: noise complaints could limit working hours on Ferry Road.
- Land: one lease at the depot site is not yet signed.

Next steps

- Recovery plan for the track works to the steering group on 14 November.
- Public drop-in sessions at the Calder Market library in the first week of November.
- Briefing for contractors on the night-work rules before work restarts on Ferry Road.
- Next steering group meeting: 9 January 2028.

Contacts

- Project director: Ana Ferreira-Holm
- Delivery office: harbourline@portcalder.example
- Questions on this update can be sent to the delivery office before the meeting.
