Website Redesign Proposal

Prepared for Northwind Bakery by Acme Studio

> **Proposal number:** NW-2026-114
> **Date:** 2 November 2026
> **Valid until:** 30 November 2026
> **Total investment:** USD 24,500

Executive summary

Northwind Bakery has grown from a single neighbourhood shop into six locations, but its website still reflects the business as it was in 2017. Customers struggle to find opening hours, the online ordering flow is difficult to use on a phone, and the content management system no longer receives security updates.

This proposal describes how Acme Studio will redesign and rebuild the website over ten weeks. The new site will make ordering fast on every device, present the bakery's story with fresh photography, and give your team a simple editor for daily specials, menus and announcements.

We recommend a phased approach: discovery and content strategy first, followed by design, development, testing and a carefully monitored launch. Each phase ends with a review meeting so that you can approve the work before we continue.

1. Background and goals

The current website was built on a commercial template that has been modified many times by different contractors. Pages load slowly, the navigation has grown to more than thirty items and several important pages are only reachable through the search box. Analytics show that 71% of visits now come from mobile devices, yet the ordering flow was designed for desktop screens.

During our initial conversations your team identified three priorities. First, customers should be able to place a pickup order in under a minute. Second, every location should have an accurate page with opening hours, directions and the current menu. Third, staff should be able to publish daily specials without asking a developer for help.

We also reviewed the support emails you shared with us. Most questions concern opening hours on public holidays, allergen information and whether a cake can be ordered for a specific date. All three can be answered directly on the website, which would reduce the time your staff spend on email and phone calls.

Success will be measured against a small number of agreed metrics: the share of orders placed on mobile, the average time to complete an order, the number of support emails per week and the page speed score reported by standard performance tools. We will capture a baseline during discovery and report progress after launch.

Several technical constraints shape the project. The ordering system is provided by a third-party point-of-sale vendor and exposes a documented interface for menus, prices and pickup slots. The new website will use this interface directly, so that prices and availability are always identical in the shops and online. Product photos and allergen data will be managed in the website's content system and linked to the vendor's product codes.

Your team also asked us to keep the existing web address and to make sure that links shared on social media over the past years continue to work. We will map every old address to its new equivalent and set up permanent redirects, so that search rankings and bookmarks are preserved when the new site goes live.

Content will be migrated in two passes. In the first pass we move the pages that are still accurate, such as the company history and the catering information, and adapt them to the new templates. In the second pass we work with your staff to rewrite the menu descriptions, the location pages and the frequently asked questions, using the language your customers actually use when they write to you.

Finally, the redesign is an opportunity to tell the Northwind story. The bakery's commitment to local flour, long fermentation and zero food waste is a genuine differentiator, and the new site should make it visible without getting in the way of customers who simply want to order.

2. Scope and pricing

The table below lists the work included in this proposal. All amounts are in US dollars and exclude sales tax. Prices are fixed for the scope described here; changes requested after design approval will be estimated separately.


Phase	Deliverables	Price (USD)
Discovery	Stakeholder interviews, analytics review, content audit	3,000
Design and prototyping	Wireframes, visual design, clickable prototype	8,000
Development	Front end, ordering integration, content management	10,500
Testing and launch	Browser testing, accessibility review, go-live support	3,000
Total		**24,500**

Payment is due in three instalments: 30% on signature, 40% on design approval and 30% on launch. Invoices are payable within 30 days of receipt.

Photography is not included. We can recommend local photographers and art-direct the shoot if required.

3. Timeline

The project will take ten weeks from the kickoff meeting to launch. The chart below shows the planned duration of each phase. Phases overlap slightly so that development can begin on approved templates while the remaining pages are still being designed.

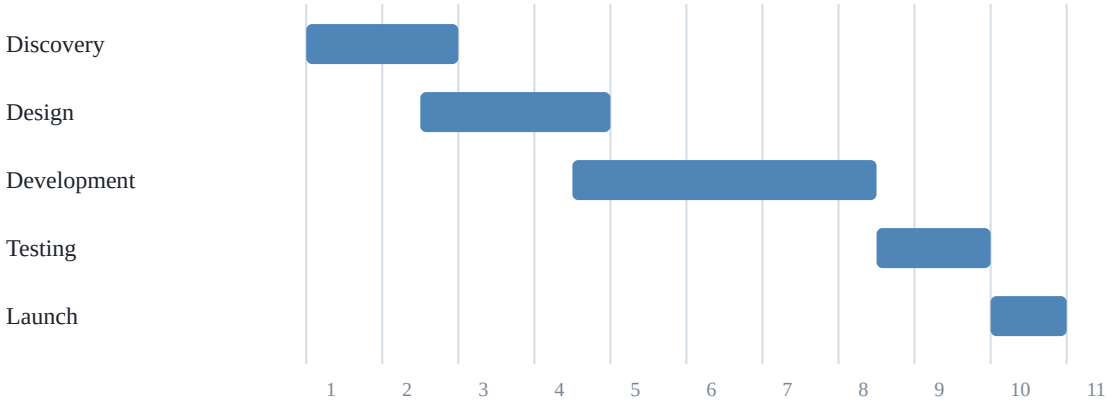

Key milestones are the content audit at the end of week two, design approval at the end of week four, a complete staging site in week eight and the public launch in week ten. We will agree exact dates at the kickoff meeting.

The timeline assumes that feedback on each deliverable is provided within three working days. Longer review periods will move the launch date accordingly.

4. Your team

A small, senior team will work on your project from start to finish. You will meet everyone at the kickoff and can reach them directly throughout the engagement.

Maya Chen — Project lead

Maya has led more than forty website projects for hospitality and food brands over the past nine years. She will be your single point of contact, run the weekly status meetings and own the delivery plan from kickoff to launch.

Tomás Rivera — Design director

Tomás is responsible for the visual language, the component library and the photography direction. He previously redesigned the online ordering experience for two regional coffee chains and a national grocery brand.

Priya Natarajan — Lead engineer

Priya will build the front end, integrate the ordering system and set up hosting, monitoring and automated backups. She is a core maintainer of two open-source accessibility libraries.

Jonas Weber — Content strategist

Jonas will audit the existing pages, interview your staff and rewrite the menu and story pages so that they are shorter, clearer and easier to find through search engines.

5. Terms and conditions

Ownership. On final payment, Northwind Bakery will own all design files, source code and content created specifically for this project. Acme Studio may show the finished website in its portfolio unless you ask us not to.

Changes to scope. Requests that fall outside the scope described in this proposal will be estimated in writing before any work begins. No additional work will be invoiced without your written approval.

Late payment. Invoices that remain unpaid **30 days** after the due date incur interest of 1.5% per month. Acme Studio may pause work on the project until overdue invoices have been settled.

Confidentiality. Both parties will keep confidential any non-public business information they recieve during the project, and will only use it for the purposes of this engagement.

Cancellation. Either party may end the agreement with 30 days written notice. Work completed up to the end of the notice period will be invoiced at the prices shown in section 2.

Warranty. We will fix defects reported within 60 days of launch at no charge. A defect is any behaviour that differs from the approved designs or the agreed functional specification.

6. Support and maintenance

After the warranty period ends, we offer an optional support plan that covers security updates, uptime monitoring, monthly backups and up to four hours of small changes per month. The plan can be cancelled at any time with one month's notice.

Support requests are answered within one business day. Urgent issues, such as the ordering system being unavailable, are handled within two hours between 7:00 and 21:00, seven days a week.

We will also run a quarterly review in which we look at analytics together, recommend improvements and plan seasonal campaigns such as holiday pre-orders.

Appendix A. Rate card

The following hourly rates apply to work outside the fixed scope and to the optional support plan.

Role	Hourly rate (USD)
Project lead	140
Design director	150
Lead engineer	145
Content strategist	110

Rates are reviewed once a year. You will be notified of any change at least 60 days in advance.
